



| W/C | 03/07 | 10/07 | 17/07 | 24/07 | 31/07 | 07/08 | 14/08 | 21/08 | 28/08 | 04/09 | 11/09 | 18/09 | 25/09 | 02/10 | 09/10 | 16/10 |
|-----|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|
| | | | | | | | | | | | | | | | | |

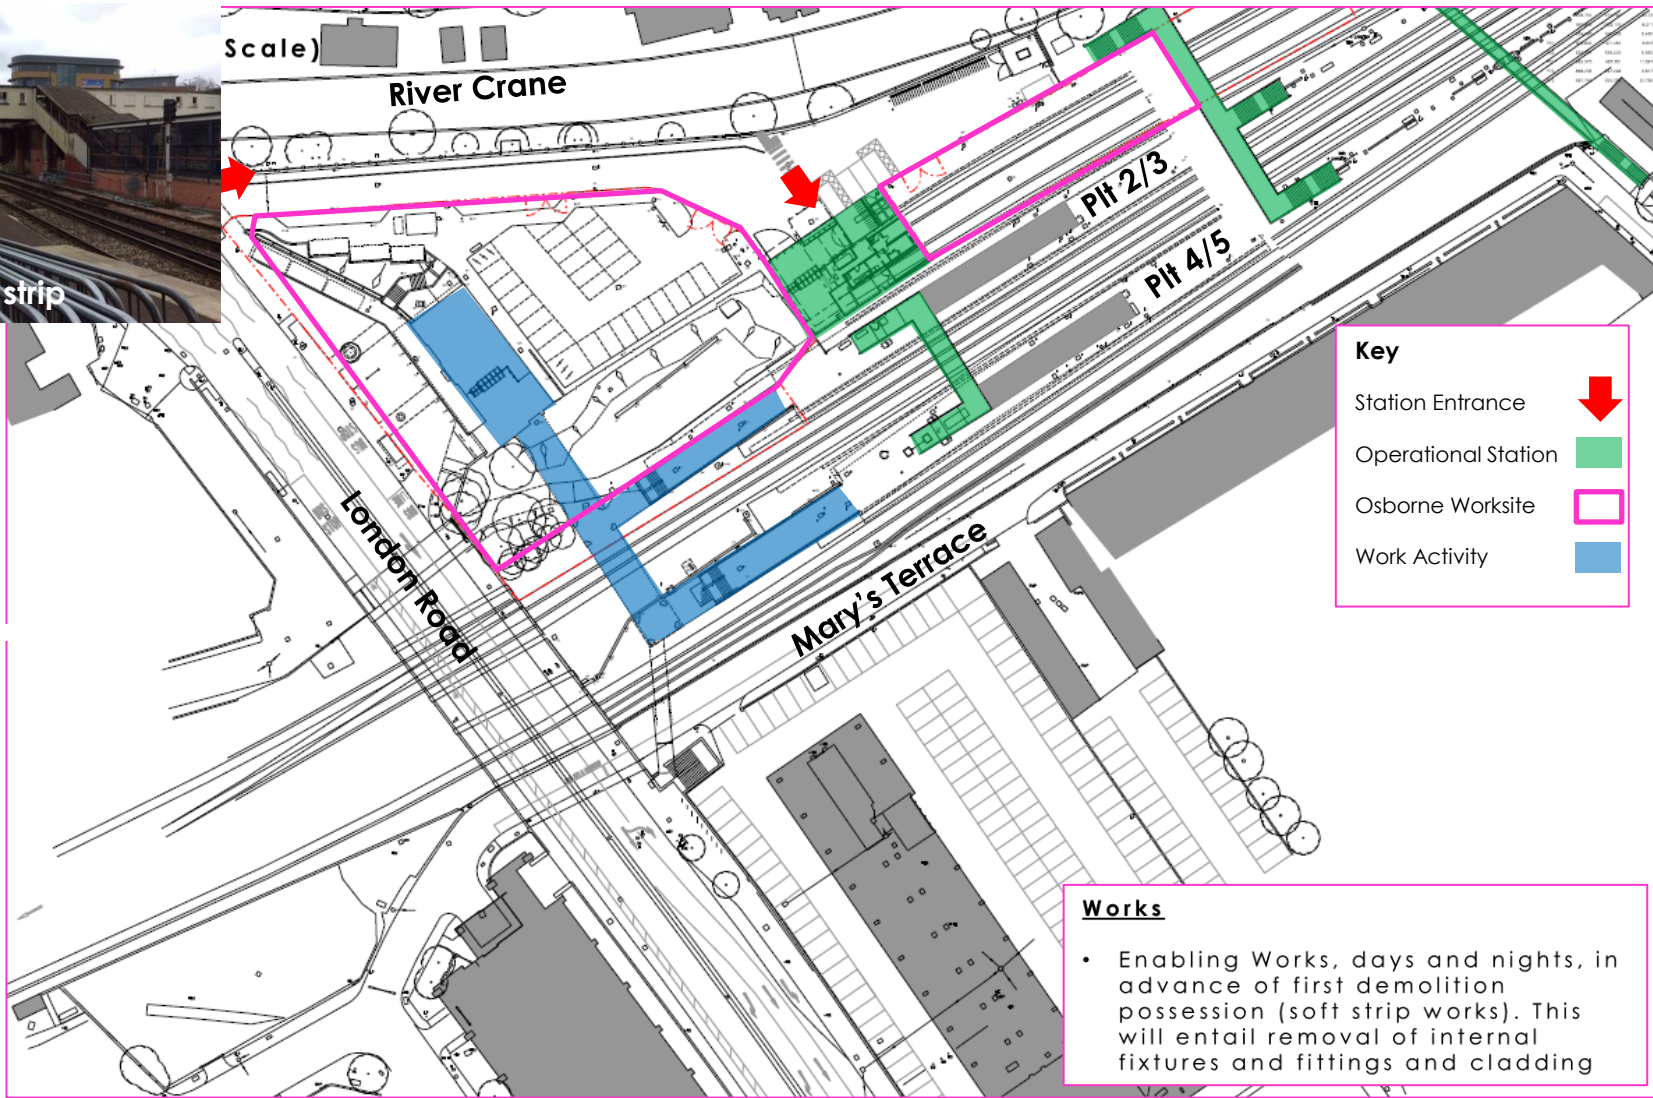

Solum Twickenham Development: Demolition Sequence

| W/C | 03/07 | 10/07 | 17/07 | 24/07 | 31/07 | 07/08 | 14/08 | 21/08 | 28/08 | 04/09 | 11/09 | 18/09 | 25/09 | 02/10 | 09/10 | 16/10 |
|-----|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|
| | | | | | | | | | | | | | | | | |

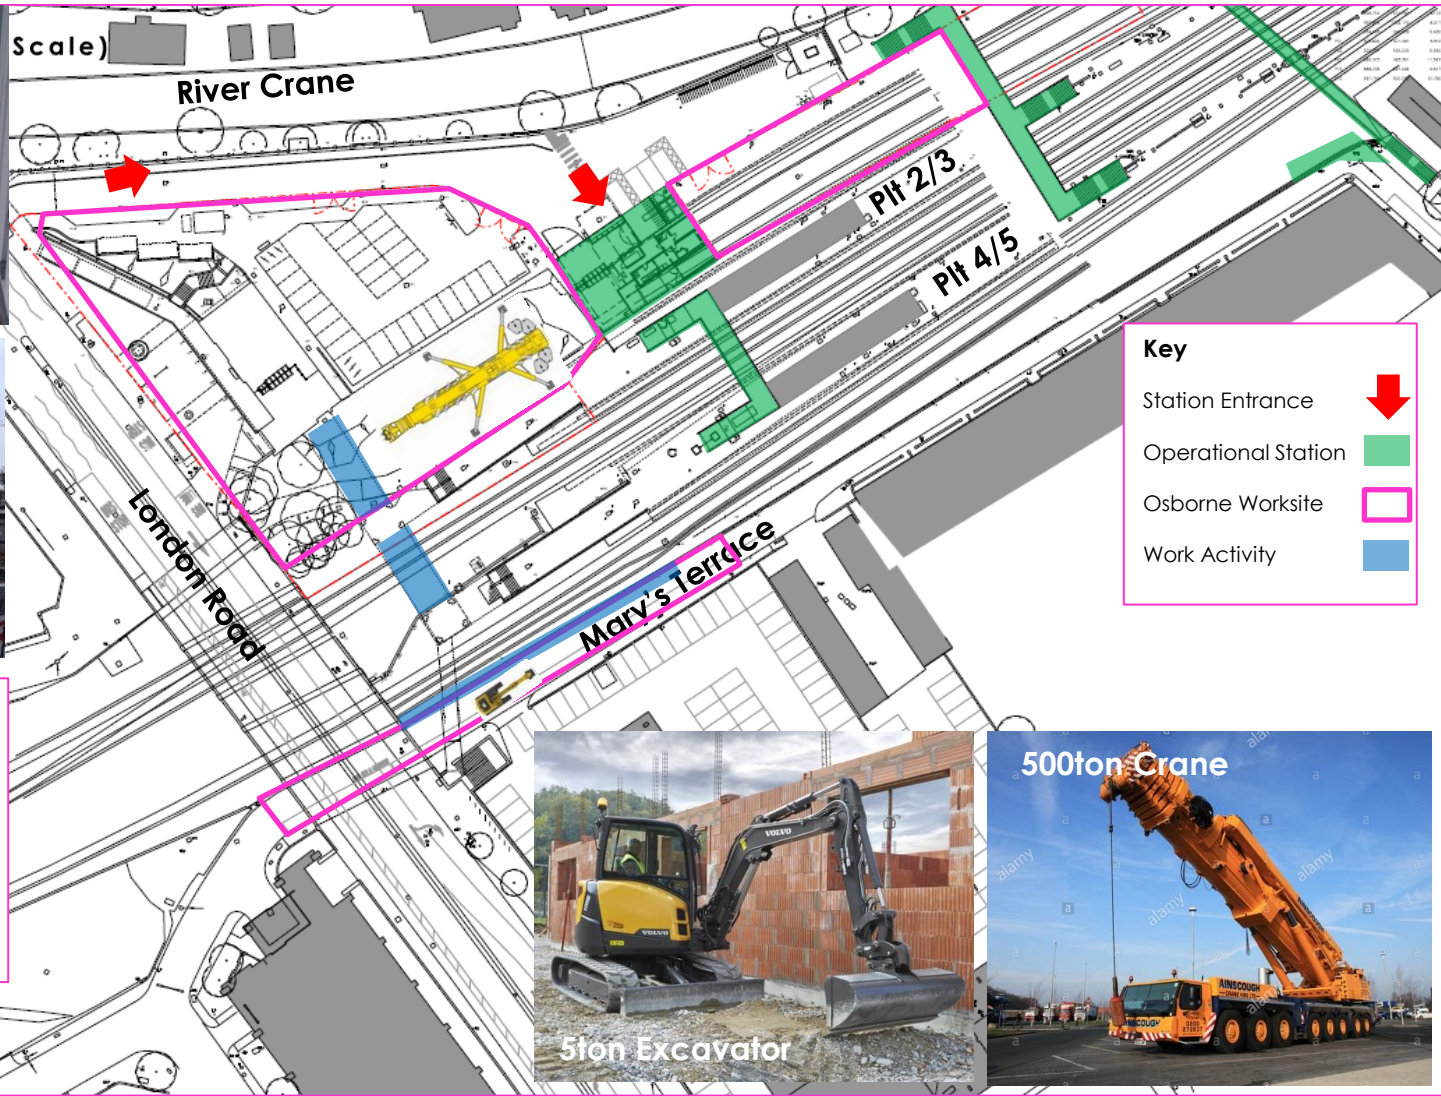

Key

- Station Entrance
- Operational Station
- Osborne Worksite
- Work Activity

Works



Possession 1 (10.09.17)
28hour

- Bridge Span Removal, using 500ton mobile crane.
- Demolition of Mary's Terrace Wall, using 5ton excavator



Solum Twickenham Development: Demolition Sequence

| W/C | 03/07 | 10/07 | 17/07 | 24/07 | 31/07 | 07/08 | 14/08 | 21/08 | 28/08 | 04/09 | 11/09 | 18/09 | 25/09 | 02/10 | 09/10 | 16/10 |
|-----|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|
| | | | | | | | | | | | | | | | | |

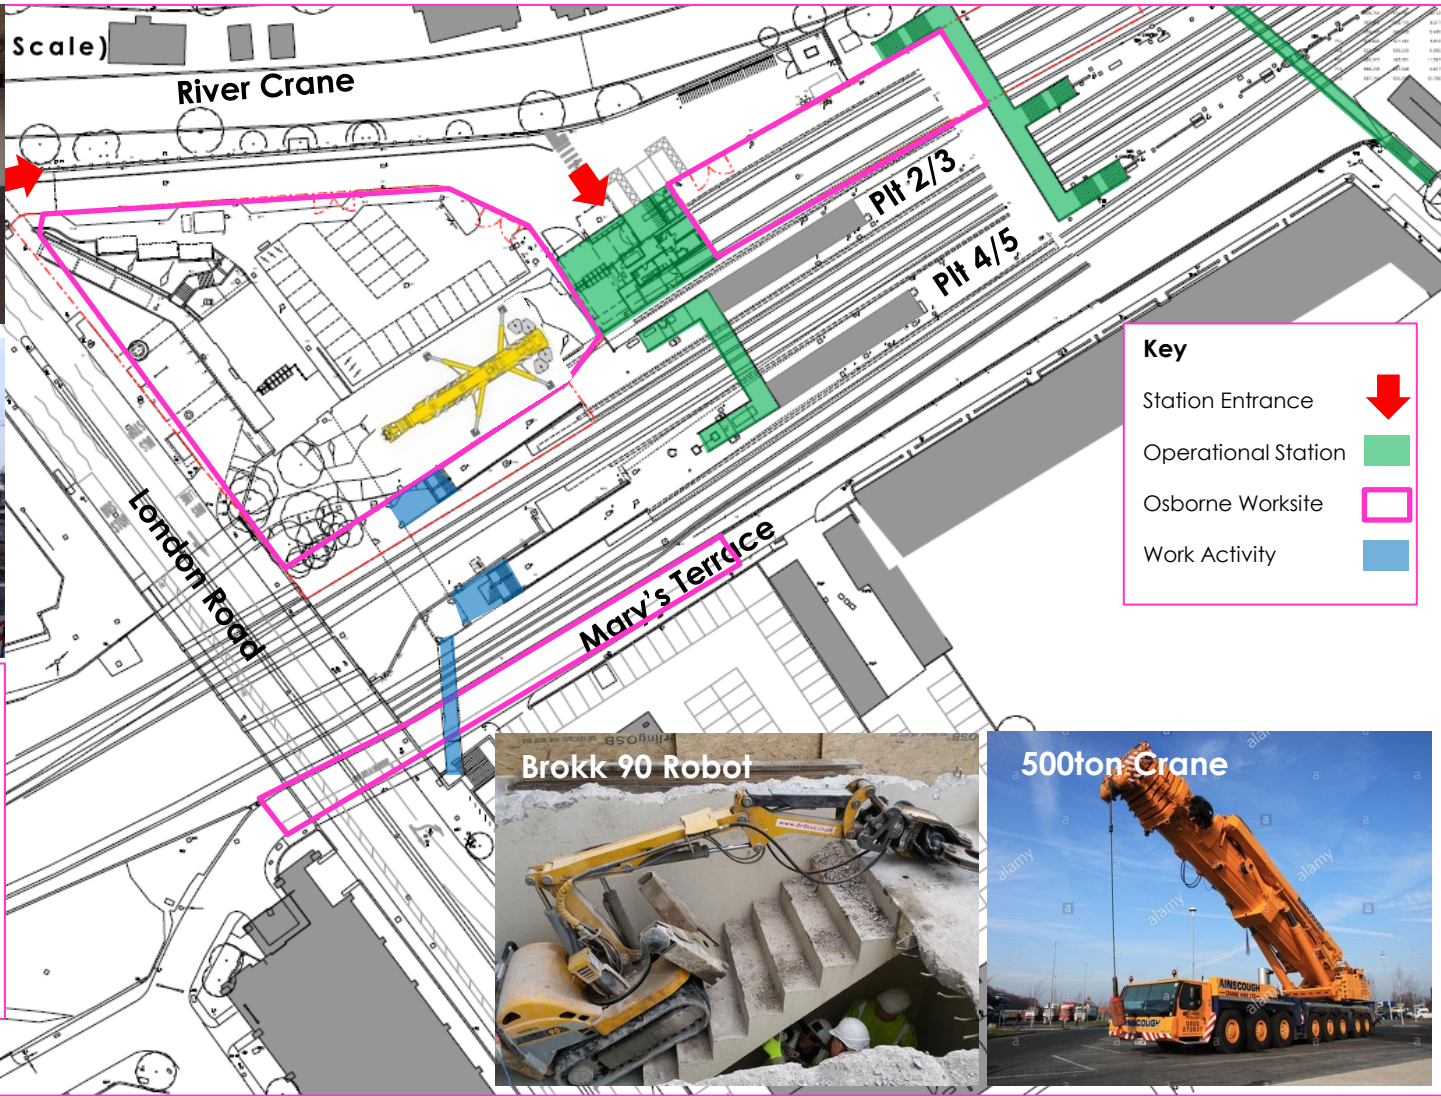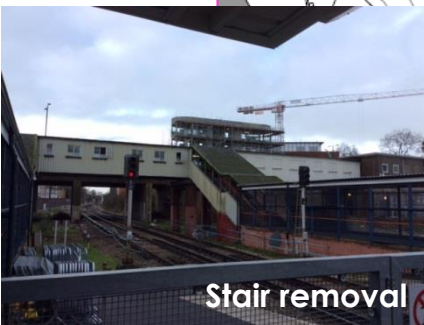

Key

- Station Entrance
- Operational Station
- Osborne Worksite
- Work Activity

Works


Possession 2 (17.09.17)
28hour

- Demolition and removal of bridge span, using 500ton crane and Brokk 90 robot. (Pavement to be closed to the public)
- Demolition and removal of stairwells using 500tone crane and Brokk 90 robot



Solum Twickenham Development: Demolition Sequence

| W/C | 03/07 | 10/07 | 17/07 | 24/07 | 31/07 | 07/08 | 14/08 | 21/08 | 28/08 | 04/09 | 11/09 | 18/09 | 25/09 | 02/10 | 09/10 | 16/10 |
|-----|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|
| | | | | | | | | | | | | | | | | |

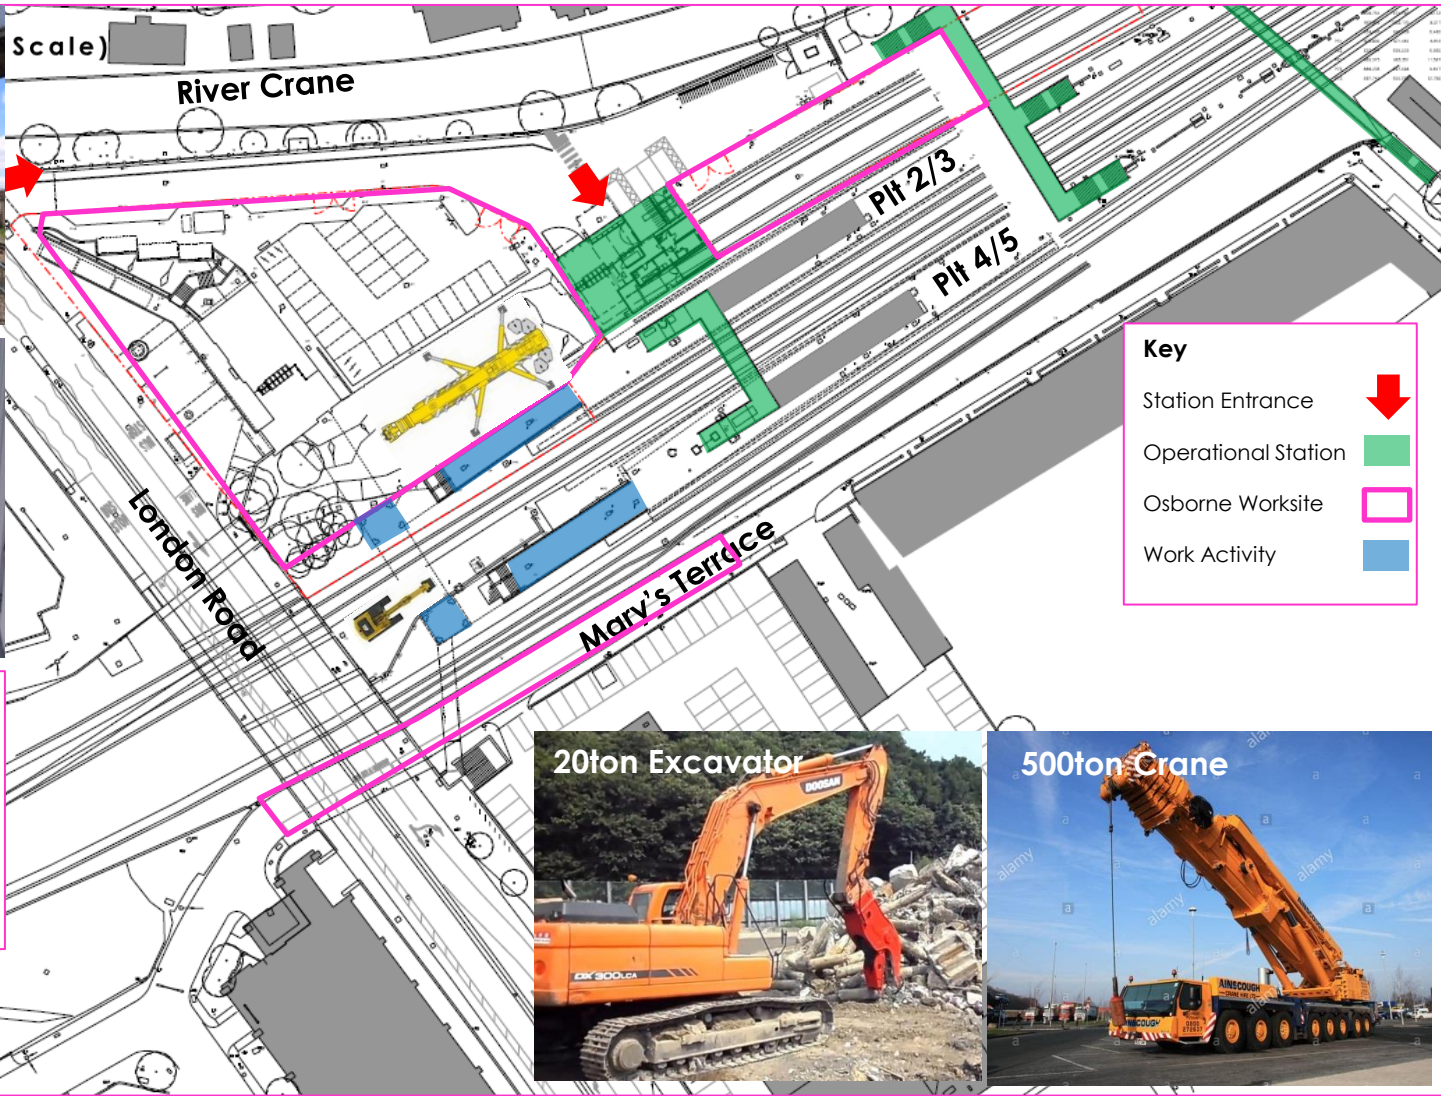

Works


Possession 3 (30.09.17)
52hour

- Demolition of Footbridge Piers and Walkways using 20ton excavator and 500ton mobile crane



Solum Twickenham Development: Demolition Sequence

| W/C | 03/07 | 10/07 | 17/07 | 24/07 | 31/07 | 07/08 | 14/08 | 21/08 | 28/08 | 04/09 | 11/09 | 18/09 | 25/09 | 02/10 | 09/10 | 16/10 |
|-----|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|
| | | | | | | | | | | | | | | | | |

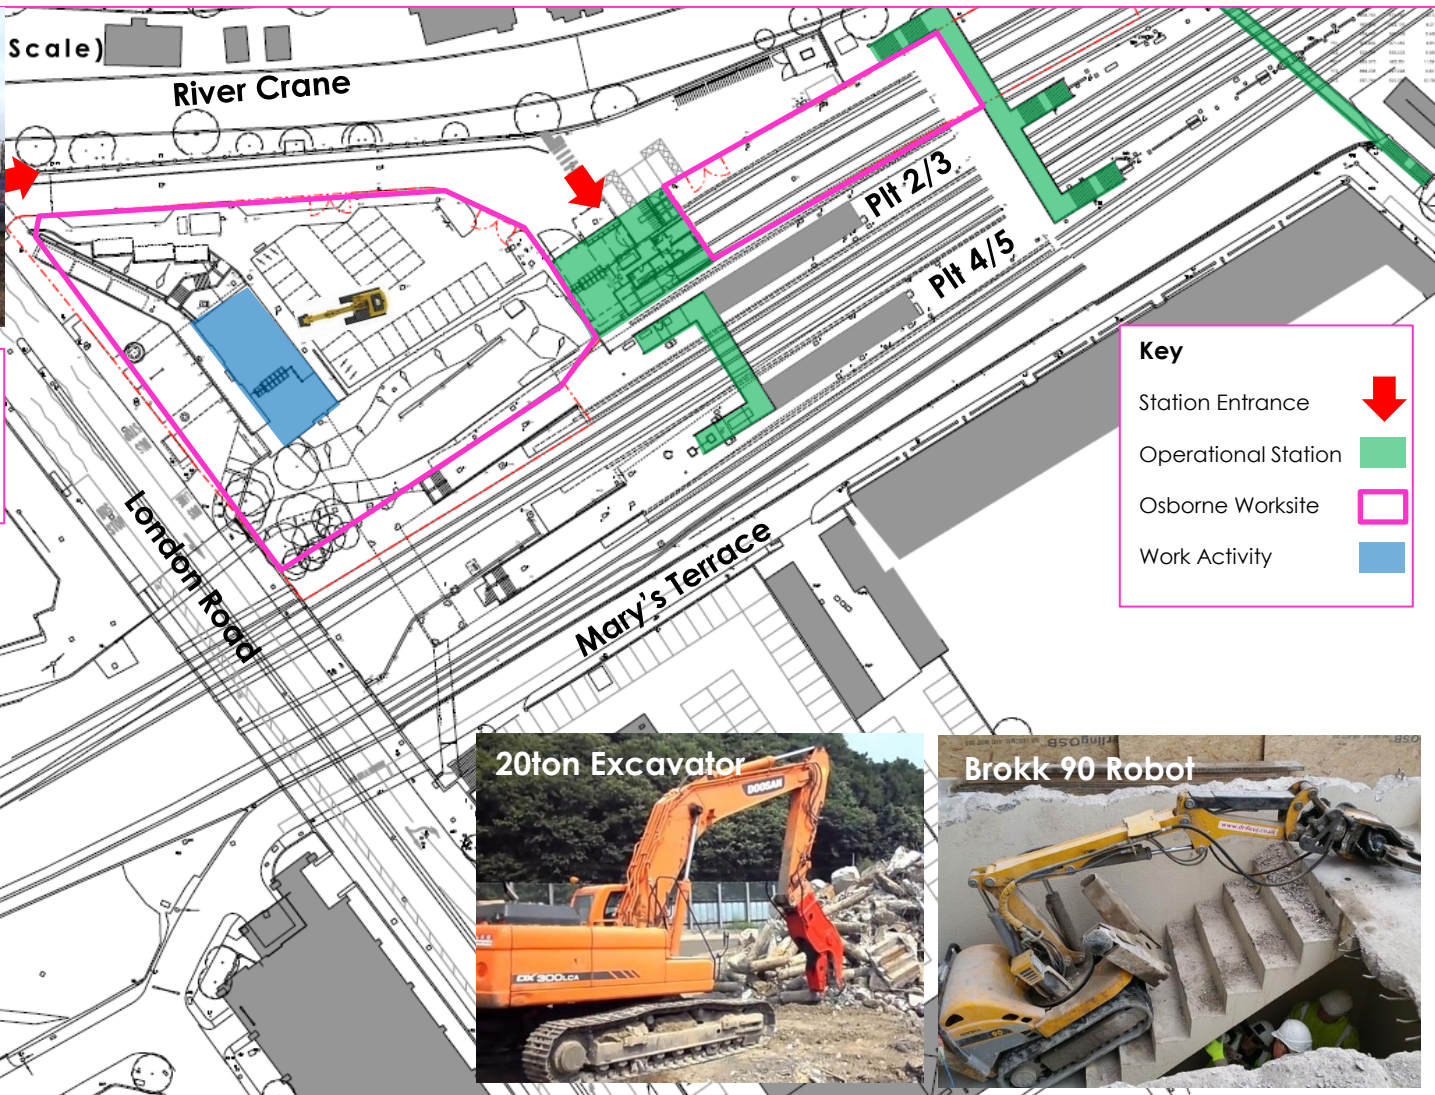

- Works**
- Demolition of old station (Days), using 20ton excavator and Brokk 90 robot



Solum Twickenham Development: Demolition Sequence
